

Multiple Sewershed Package 18 Project

Non-Mandatory WebEx Pre-Bid Meeting

October 28, 2021

Alla Korostyshevsky, P.E., PMP

Pipelines – SSO Condition and Water Projects

Janie Powell


Contract Administrator

Marisol V. Robles

SMWVB Program Manager

Michael Persyn, PE

K Friese + Associates, Engineer of Record



MAKING SAN ANTONIO
WATERFUL




Project Update

- Location 5 Leon Creek
 - Sewer collapse on 54", 66", and 72" pipes in late October 2021




Project Update

- Emergency declared
 - Bypass contractor NTP 10/23/21
 - Open cut contractor NTP expected about 11/4/21
- Replacement of damaged sections anticipated complete not later than end of February 2022
- Prospective bidders are strongly encouraged to revisit the site, ensure they are familiar with conditions, and to review emergency plans for information

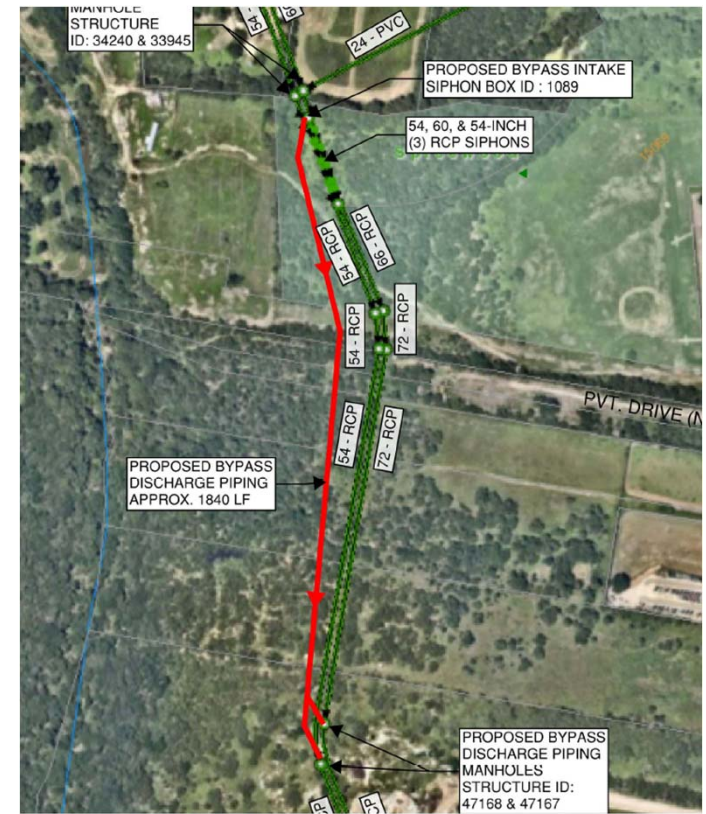

Emergency Project Scope

- ~ 75 MGD bypass
- ~867 LF 54" & 72" open cut (replace existing RCP)
 - 1011927
 - 1021470
 - 1012022
 - 1021821

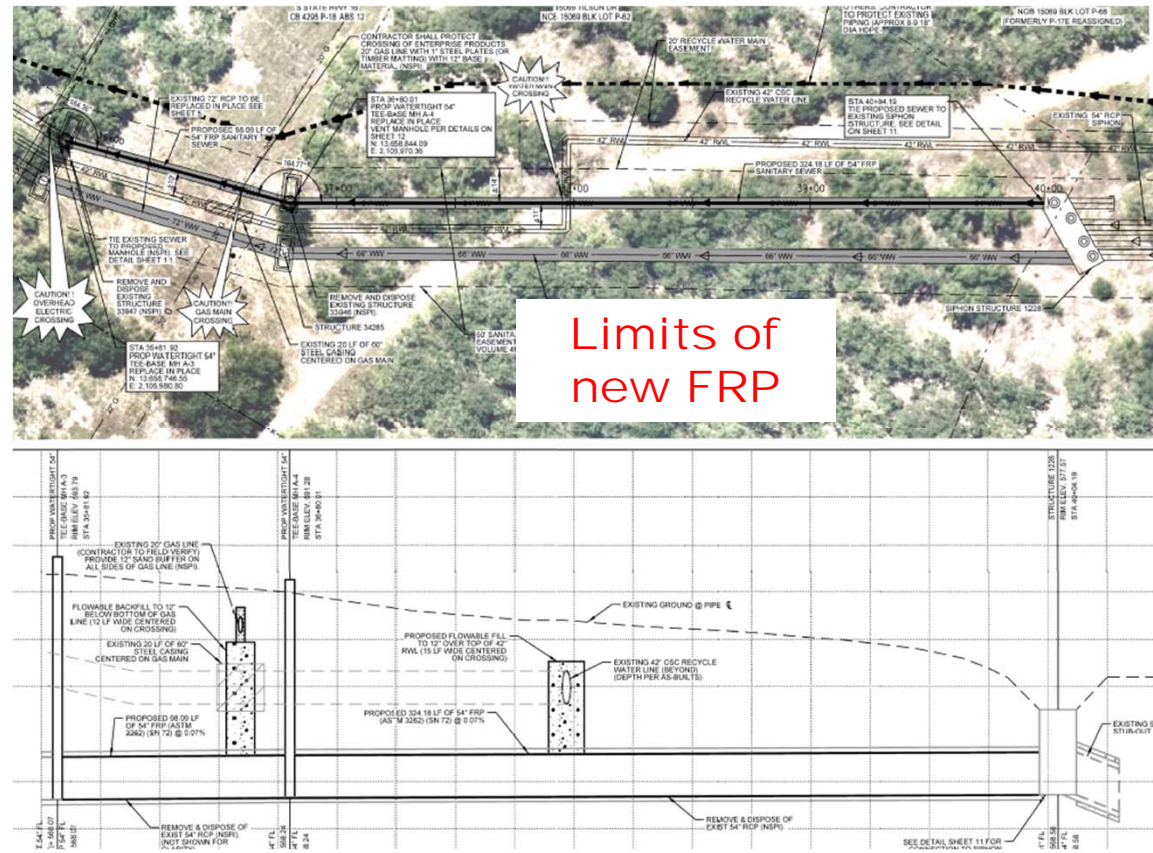

Multiple Sewershed Package 18



Project Impacts

- Added contractor coordination
 - Open cut contractor may be demobilizing
 - Bypass contractor may be removing bypass in March 2022
- Portions of haul route cleared and roadway constructed from RLCA property to COSA parks property
 - Pkg 18 required to restore the site at the end of construction



Project Impacts

- Minor reduction in 54"/66" CIPP (~325 LF each)
 - May require lining through new FRP pipe
- New tee-base manholes
 - MH 34285, MH 34286, MH 33946, MH 33947




Project Impacts

- Significant debris in pipes downstream – bid accordingly
 - Limited CCTV available; will be made available

MH 47167 - Looking Upstream



MH 34286 - Looking Downstream

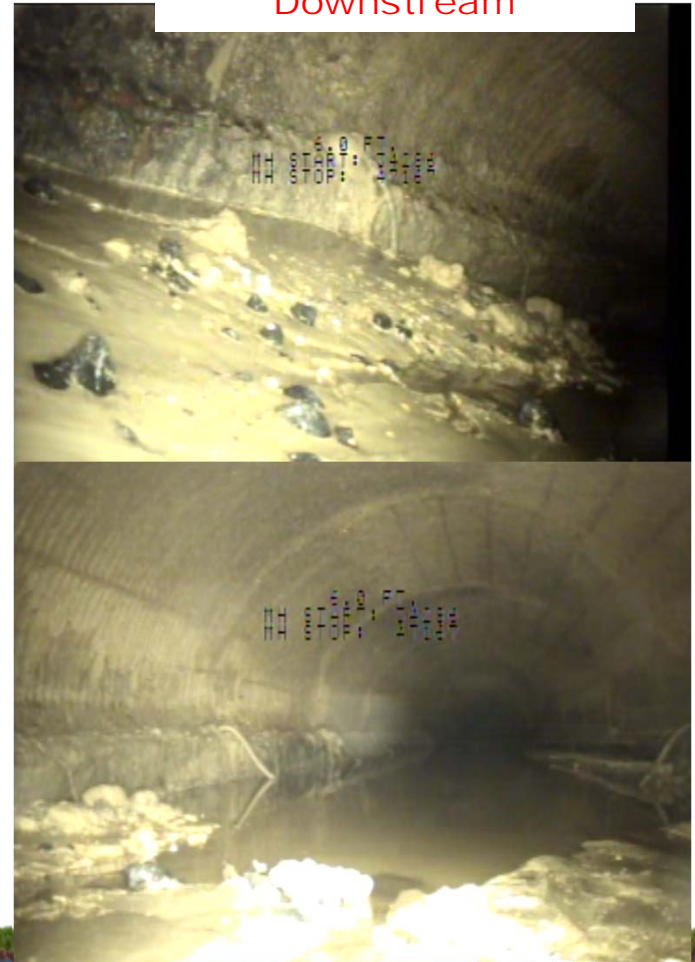

Contact Information

<u>Contact Name</u>	<u>Title</u>	<u>Telephone Number</u>	<u>Email address</u>
Janie Powell	Contract Administrator	210-233-2443	Janie.Powell@saws.org
Marisol V. Robles	SMWVB Program Manager	210-233-3420	Marisol.Robles@saws.org

REMINDER

Please be advised that Bidders are prohibited from communicating with any other SAWS staff, the Consultant, the Developer, or City of San Antonio officials regarding this IFB up until the contract is awarded as outlined in the Instructions to Bidders

QUESTIONS



Reminder: Oral statements or discussion during the pre-bid meeting today will not be binding, nor will it change or affect the terms or conditions within the Plans and Specifications of this Project. Changes, if any, will be addressed in writing only via an Addendum.
